



# Illinois Department of Natural Resources

One Natural Resources Way Springfield, Illinois 62702-1271  
www.dnr.illinois.gov


Bruce Rauner, Governor  
Wayne A. Rosenthal, Director

## Fox River Status Update February 8, 2019

### Current Conditions

Most of the Fox River watershed received about 0.1” to ¼” of precipitation as shown on Figure 1. Measured inflows on the Fox River near New Munster, WI are 2480 cfs and appears to be cresting; flows on Nippersink Creek near Spring Grove are 699 cfs and appears to be cresting. The Fox Lake stage is 4.38 ft and the Stratton Dam Tailwater stage is 4.23 ft. The Fox River at the Algonquin Dam Tailwater stage is 8.91 ft. Please note that the freezing air temperatures may affect the river gages.


Figure 1: Observed Precipitation

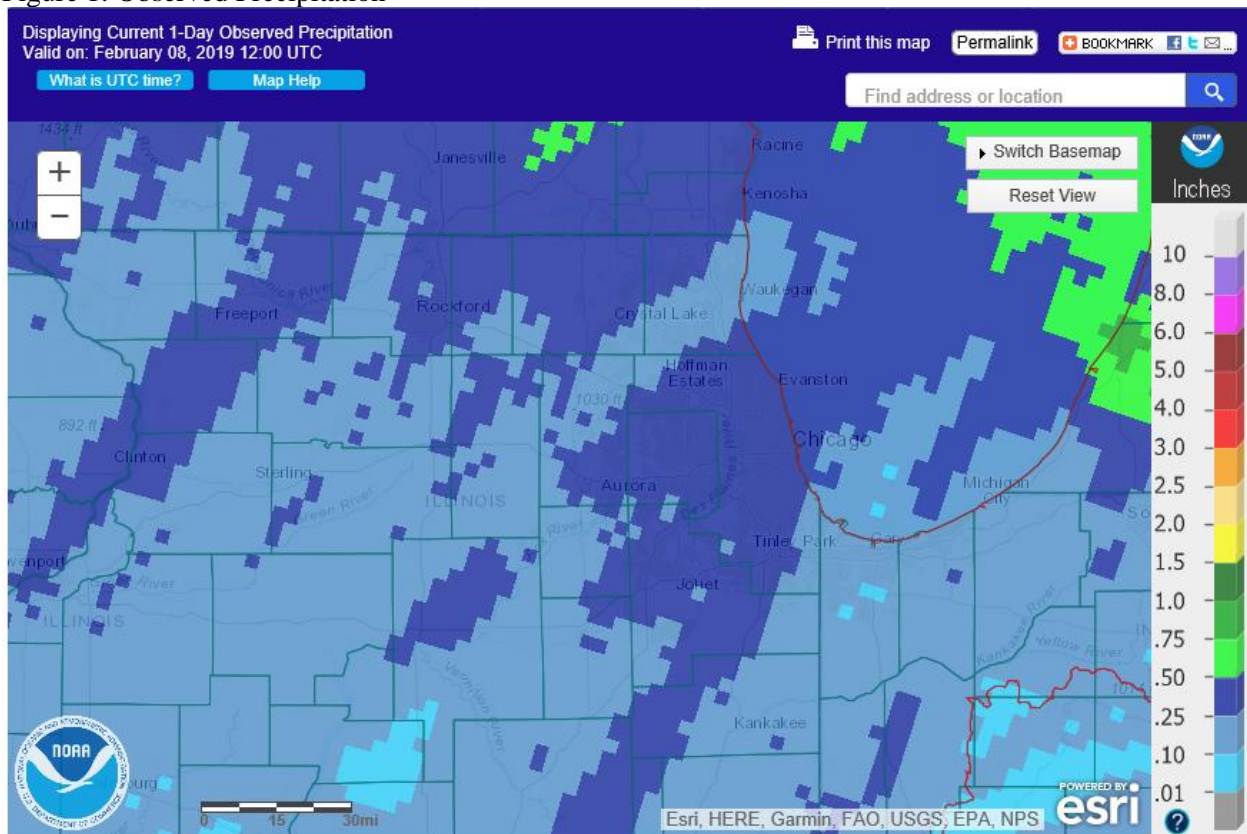

## Forecast

The National Weather Service (NWS) is predicting frozen precipitation for the next 5 days in the Fox River watershed. Figure 2 shows that the Fox River watershed may receive ¼” to ½” of precipitation in the next 5 days. The NWS is forecasting the Fox River at Algonquin Tailwater will crest at a stage of 9.2 feet on February 10<sup>th</sup> with a flow of 3400 cfs.

Figure 2: Forecasted Rainfall for the Next 5 days

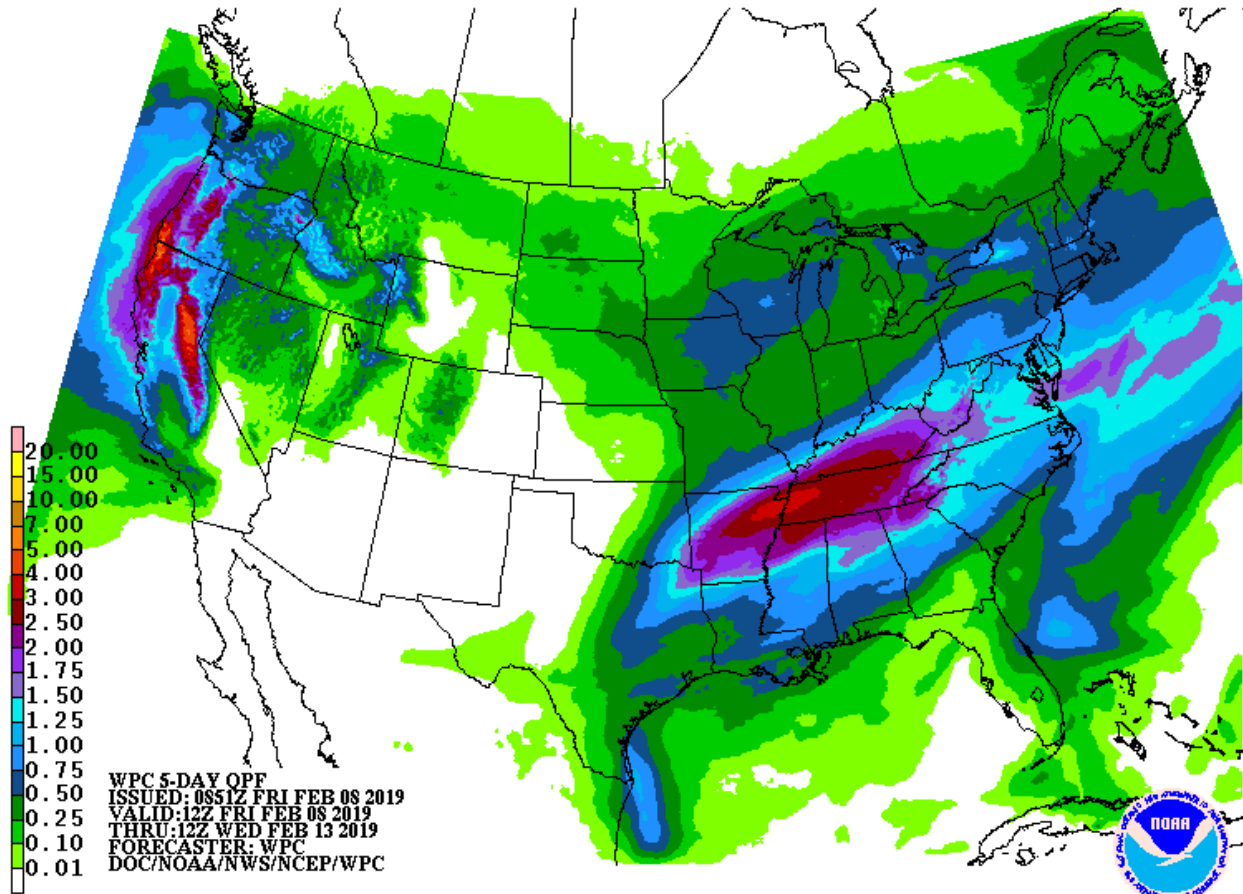

## System Conditions and Operations

The sluice gates and the hinged crest gate at Stratton Dam are opened. The hinged crest gate at Algonquin Dam is partially opened. Estimates indicate that the Stratton Dam tailwater may crest at 4.6’ and the Chain of Lakes may crest at 4.7’ on February 11<sup>th</sup>. Our goal is to continue moving as much flow as possible the next few days without impacting homes.

Munib Ahmad, P.E.

Office of Water Resources

Illinois Department of Natural Resources

<https://www.dnr.illinois.gov/WaterResources/Pages/StrattonLockandDam.aspx>
