



# Illinois Department of Natural Resources

One Natural Resources Way Springfield, Illinois 62702-1271  
www.dnr.illinois.gov

JB Pritzker, Governor


Colleen Callahan, Director

## Fox River Status Update October 4, 2019

### Current Conditions

Fox River watershed received little or no precipitation within the last 24 hours as shown on Figure 1. Measured inflows on the Fox River near New Munster, WI are 4240 cfs and levelling off; flows on Nippersink Creek near Spring Grove are 1540 cfs and levelling off. The Fox Lake stage is 5.7 ft and the Stratton Dam Tailwater stage is 5.13 ft. The Fox River at the Algonquin Dam Tailwater stage is 10.06 ft.


Figure 1: Observed Precipitation

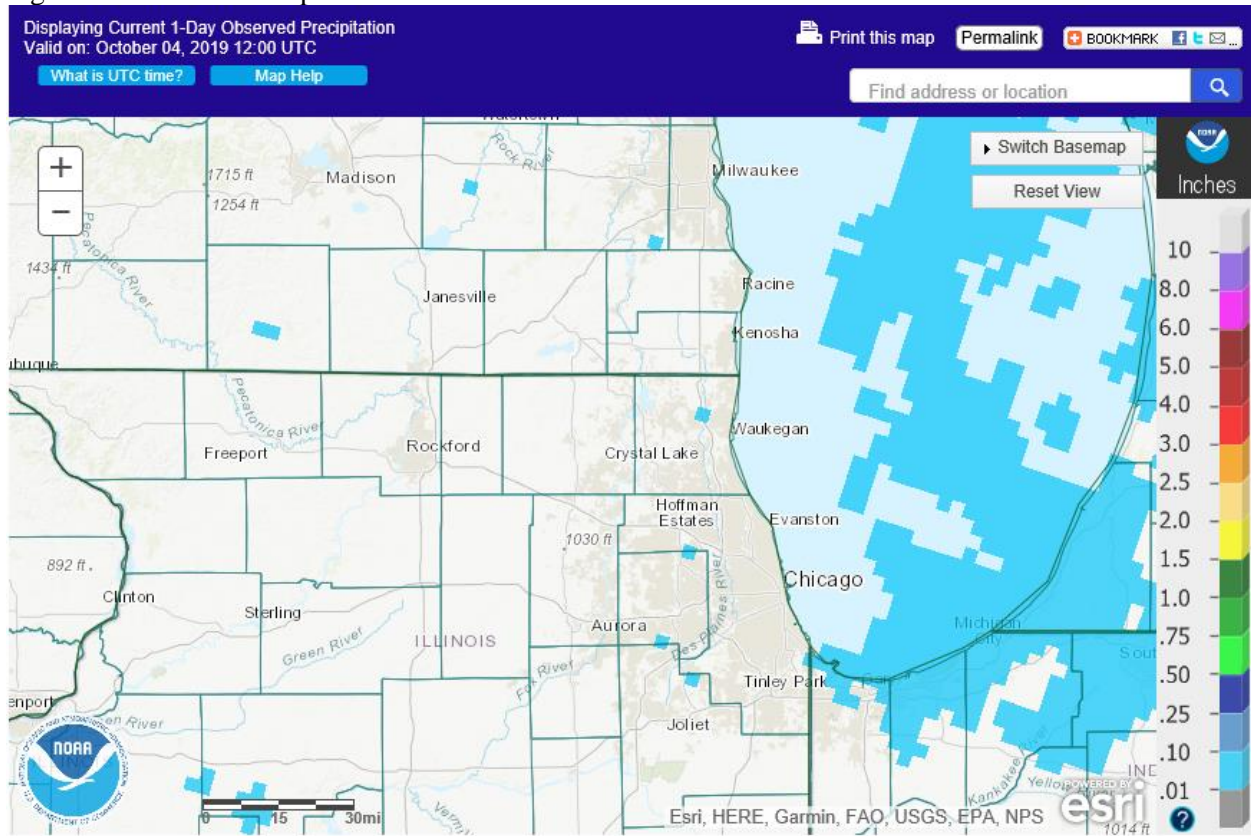

### Forecast

The National Weather Service (NWS) is predicting 0.1” to ½” of precipitation for the next 3 days in the Fox River watershed as shown on Figure 2. The NWS is forecasting that the Fox River near New Munster, WI will crest at a stage of 13.7 ft on October 5<sup>th</sup>. The NWS is forecasting that the Fox River at Algonquin Tailwater will crest at a stage of 11.0 ft on October 7<sup>th</sup> with a flow of 5250 cfs.

Figure 2: Forecasted Precipitation for the Next 3 days

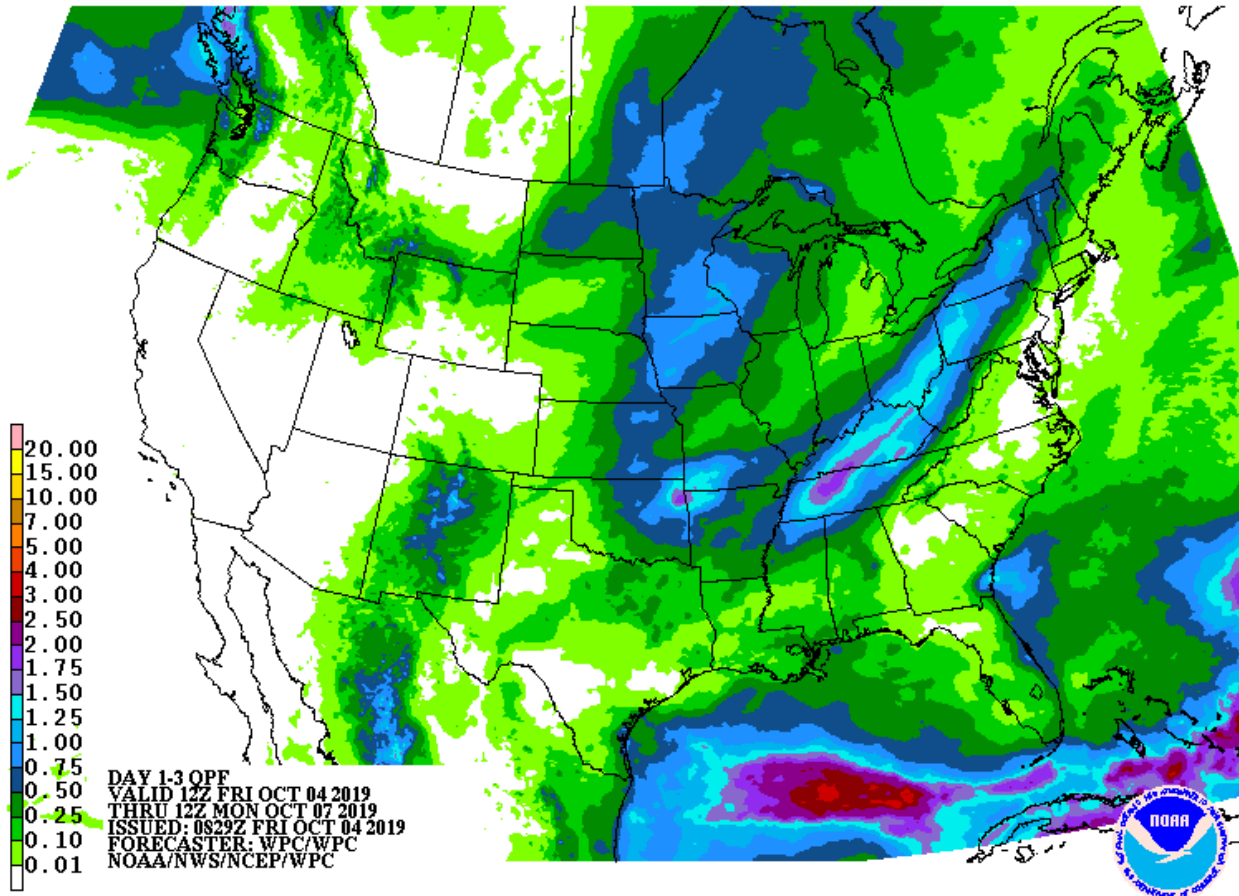

### System Conditions and Operations

All gates at Stratton Dam and Algonquin Dam are opened to pass as much flow as possible. Based on today’s river forecast from the NWS, our estimates indicate that Fox Lake and Stratton Dam Tailwater may crest near 6.2 ft on Sunday/Monday.

Munib Ahmad, P.E.

Office of Water Resources

Illinois Department of Natural Resources

<https://www.dnr.illinois.gov/WaterResources/Pages/StrattonLockandDam.aspx>
